






Activity ID	Description	Rem Dur	Early Start	Early Finish
0060	Design and Engineering	60	01/23/07	04/16/07
0062	DSA Approval	90	01/23/07	05/28/07
0061	Submittals (including Ext./Int.)	30	02/13/07	03/26/07
0063	Shop Fabrication	38	03/05/07	06/07/07
0064	Transport Floors (Friday)	1	06/08/07	06/08/07
0065	Pick and Set Floors (Saturday)	1	06/11/07	06/11/07
0066	Assembly Office Building	5	06/12/07	06/18/07
0067	Assembly Storage Building	3	06/12/07	06/14/07
0068	Roofing	2	06/19/07	06/20/07
0069	Exterior Skin / Finishes	22	06/19/07	07/18/07
0070	Interior Build-out / Finishes	50	06/19/07	08/27/07
0072	MPE Tie-ins	5	06/19/07	06/25/07
0071	Low Voltage Systems	10	07/31/07	08/13/07
0073	Start-up and Testing	3	08/21/07	08/23/07

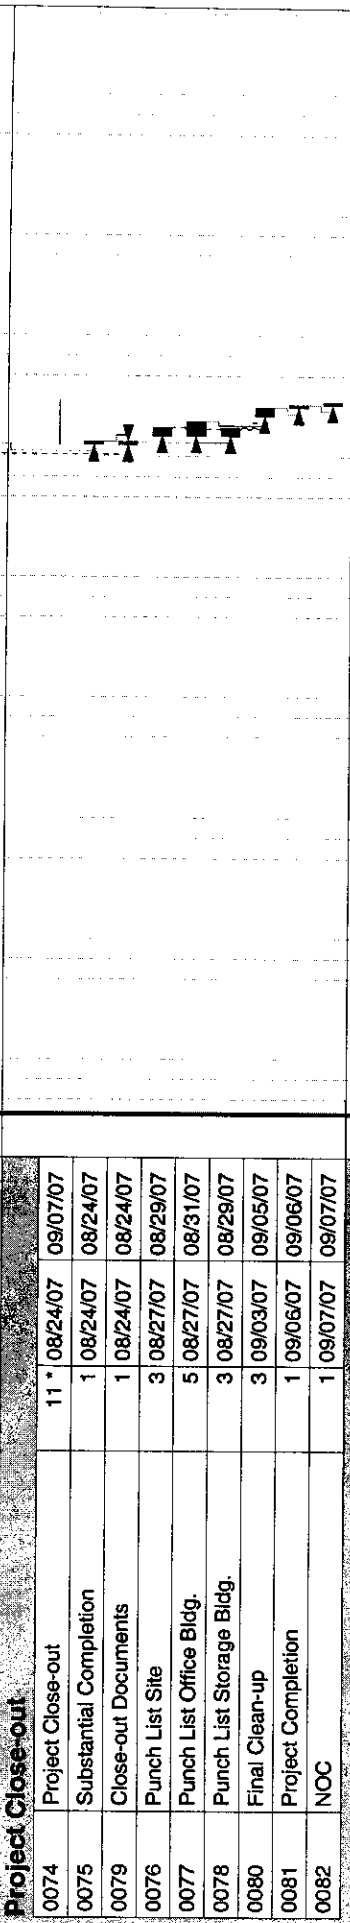

Activity ID	Description	Rem Dur	Early Start	Early Finish
<b>Project Close-out</b>				
0074	Project Close-out	11 *	08/24/07	09/07/07
0075	Substantial Completion	1	08/24/07	08/24/07
0079	Close-out Documents	1	08/24/07	08/24/07
0076	Punch List Site	3	08/27/07	08/29/07
0077	Punch List Office Bldg.	5	08/27/07	08/31/07
0078	Punch List Storage Bldg.	3	08/27/07	08/29/07
0080	Final Clean-up	3	09/03/07	09/05/07
0081	Project Completion	1	09/06/07	09/06/07
0082	NOC	1	09/07/07	09/07/07
<b>ADDITIVE ALTERNATE #1</b>				
0087	ADDITIVE ALTERNATE #1	0	02/19/07	04/20/07
0107	Relocate Pull Boxes	0	02/20/07	02/22/07
0117	Survey	0	02/22/07	02/22/07
0097	Demo, Clear and Grub	0	02/23/07	03/02/07
0127	Earthwork, Over-Ex	0	03/05/07	03/09/07
0128	Facilities Delay, Underground Work	0	03/08/07	03/20/07
0129	Continued E-Work, South Ramp	0	03/12/07	03/16/07

Start date 01/01/07 12:00AM  
 Finish date 09/07/07 4:59PM  
 Data date 01/03/07 12:00AM  
 Run date 04/11/07 11:00AM  
 Page number 3A

© Primavera Systems, Inc.

**ELAC Physical Plant Bldg.  
 AMG & Associates, Inc.  
 Project No.: 01-07004**

Early bar  
 Progress bar  
 Critical bar  
 Summary bar  
 Progress point  
 Critical point  
 Summary point  
 Start milestone point  
 Finish milestone point

