



















Sweet & Sassy Salon

ID	Task Name	Duration	Start	Finish	Jul 15, '07							Jul 22, '07							
					W	T	F	S	S	M	T	W	T	F	S	S	M	T	
1	Sweet and Sassy Salon	50 days	Mon 7/16/07	Fri 9/21/07															
2	Demo	6 days	Mon 7/16/07	Mon 7/23/07															
3	Saw Cut Break and Remove	2 days	Mon 7/16/07	Tue 7/17/07															
4	Remove existing duct	1 day	Mon 7/23/07	Mon 7/23/07															
5	Remove existing light fixtures	1 day	Wed 7/18/07	Wed 7/18/07															
6	Underground Utilities	5 days	Mon 7/16/07	Fri 7/20/07															
7	Rough in waste	3 days	Mon 7/16/07	Wed 7/18/07															
8	Inspection (City)	1 day	Wed 7/18/07	Wed 7/18/07															
9	Backfill / and Dowels	1 day	Thu 7/19/07	Thu 7/19/07															
10	Patch Concrete	1 day	Fri 7/20/07	Fri 7/20/07															
11	Framing	5 days	Mon 7/23/07	Fri 7/27/07															
12	Wall and Soffit Layout	1 day	Mon 7/23/07	Mon 7/23/07															
13	Start Framing	5 days	Mon 7/23/07	Fri 7/27/07															
14	Electrical	35 days	Mon 7/30/07	Fri 9/14/07															
15	Rough in Electrical	5 days	Mon 7/30/07	Fri 8/3/07															
16	Pull wire	3 days	Mon 8/6/07	Wed 8/8/07															
17	Install Light Fixtures	3 days	Wed 9/12/07	Fri 9/14/07															
18	Inspection (City)	1 day	Thu 8/9/07	Thu 8/9/07															
19	Set Trim	2 days	Wed 9/12/07	Thu 9/13/07															
20	Plumbing	31 days	Mon 8/6/07	Mon 9/17/07															
21	Rough in walls	5 days	Mon 8/6/07	Fri 8/10/07															
22	Inspection (City)	1 day	Mon 8/13/07	Mon 8/13/07															
23	Coronation	1 day	Mon 9/17/07	Mon 9/17/07															
24	Set fixtures	3 days	Wed 9/12/07	Fri 9/14/07															
25	HVAC	41 days	Tue 7/24/07	Tue 9/18/07															
26	Install New Duct	1 day	Tue 7/24/07	Tue 7/24/07															
27	Inspection (City)	1 day	Wed 7/25/07	Wed 7/25/07															
28	Air balance	1 day	Tue 9/18/07	Tue 9/18/07															
29	Drywall/Taping/Paint	24 days	Thu 8/9/07	Tue 9/11/07															
30	1 Side	5 days	Thu 8/9/07	Wed 8/15/07															

Project: Sweet and Sassy Salon Date: Wed 7/18/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


Sweet & Sassy Salon







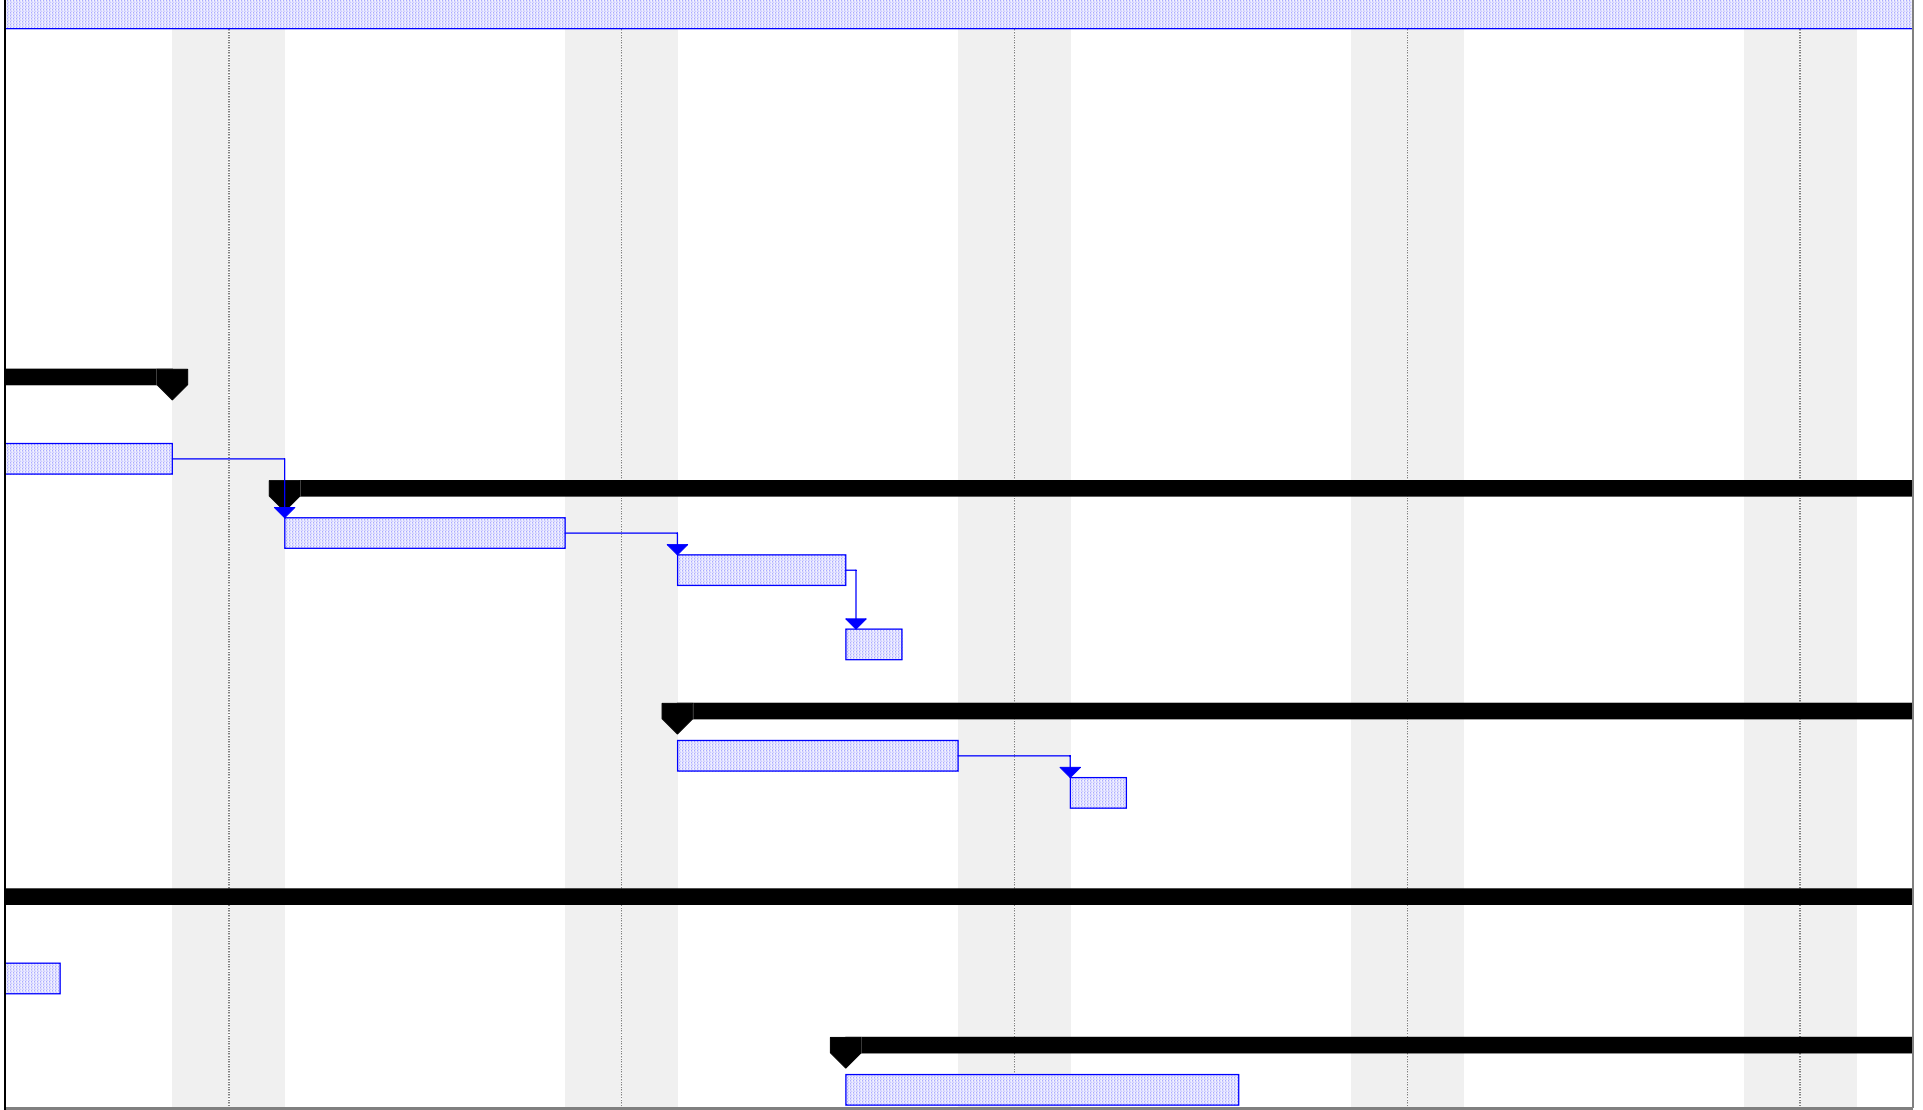


ID	Task Name	Duration	Start	Finish	Jul 15, '07							Jul 22, '07						
					W	T	F	S	S	M	T	W	T	F	S	S	M	T
31	Complete Drywall	5 days	Fri 8/17/07	Thu 8/23/07														
32	Inspection (City)	1 day	Fri 8/24/07	Fri 8/24/07														
33	Taping walls	7 days	Mon 8/27/07	Tue 9/4/07														
34	Start Painting	5 days	Wed 9/5/07	Tue 9/11/07														
35	T-Bar	5 days	Tue 9/11/07	Mon 9/17/07														
36	Start t-bar	1 day	Tue 9/11/07	Tue 9/11/07														
37	Drop Tiles	2 days	Fri 9/14/07	Mon 9/17/07														
38	Fire Protection	3 days	Wed 9/12/07	Fri 9/14/07														
39	Install new sprinklers	2 days	Wed 9/12/07	Thu 9/13/07														
40	Inspection (City)	1 day	Fri 9/14/07	Fri 9/14/07														
41	Flooring	6 days	Wed 9/12/07	Wed 9/19/07														
42	Prep floor	2 days	Wed 9/12/07	Thu 9/13/07														
43	Install new vct	4 days	Fri 9/14/07	Wed 9/19/07														
44	Furniture	4 days	Tue 9/18/07	Fri 9/21/07														
45	Install Furniture	4 days	Tue 9/18/07	Fri 9/21/07														
46	Owners Acceptance	5 days	Mon 9/24/07	Fri 9/28/07														
47	Cleanup	1 day	Mon 9/24/07	Mon 9/24/07														
48	Job Walk	1 day	Tue 9/25/07	Tue 9/25/07														
49	Punchlist	2 days	Wed 9/26/07	Thu 9/27/07														
50	Demobilization	1 day	Fri 9/28/07	Fri 9/28/07														

Project: Sweet and Sassy Salon Date: Wed 7/18/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


Sweet & Sassy Salon







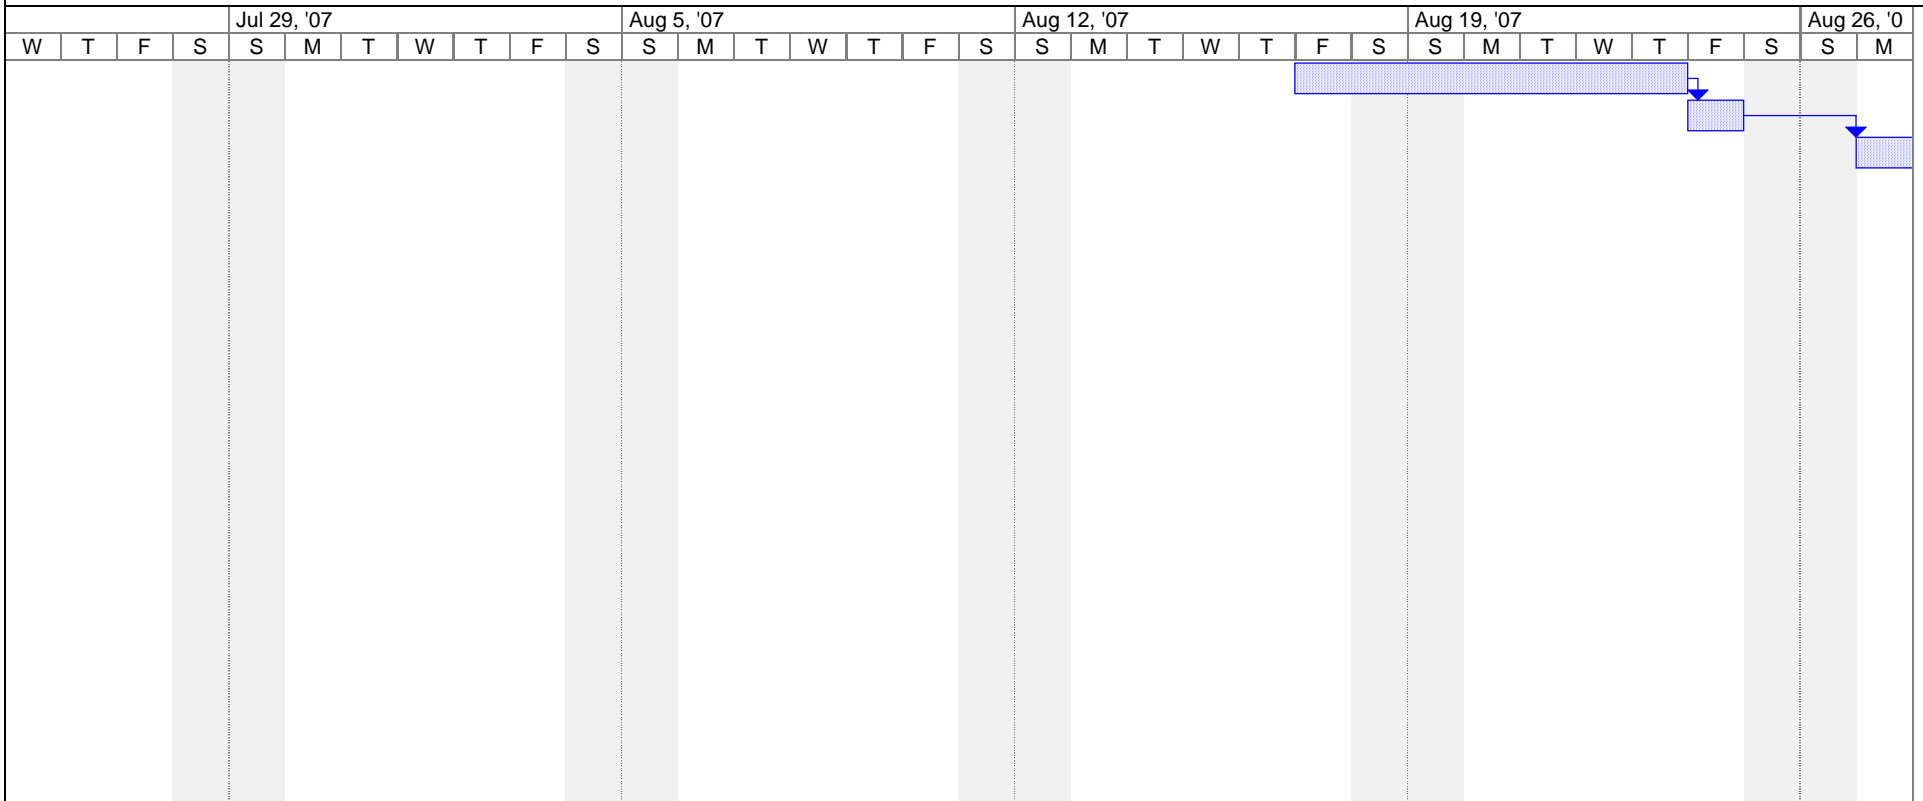


				Jul 29, '07							Aug 5, '07							Aug 12, '07							Aug 19, '07							Aug 26, '0	
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M




Project: Sweet and Sassy Salon Date: Wed 7/18/07	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

Sweet & Sassy Salon



Project: Sweet and Sassy Salon Date: Wed 7/18/07	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 


Sweet & Sassy Salon

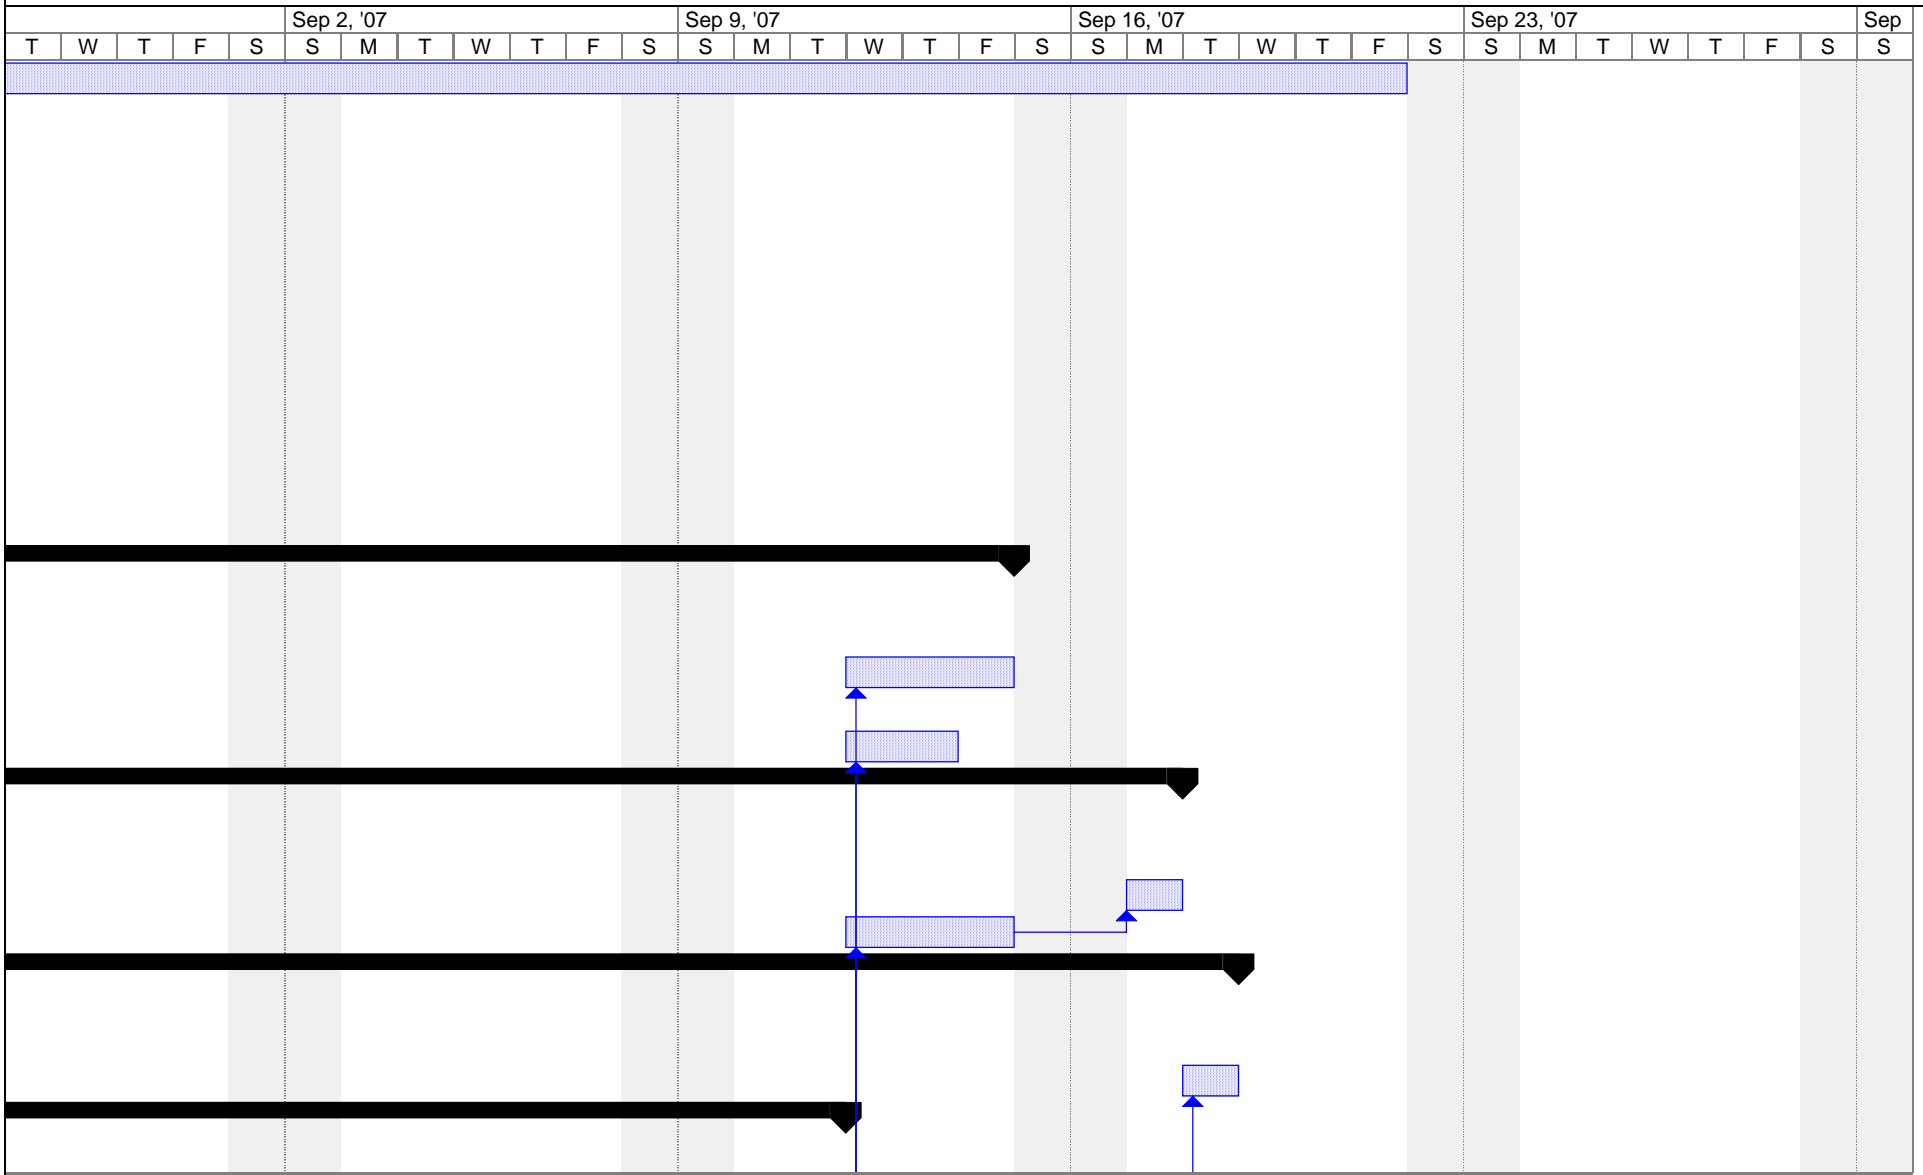

Project: Sweet and Sassy Salon
 Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Sweet & Sassy Salon

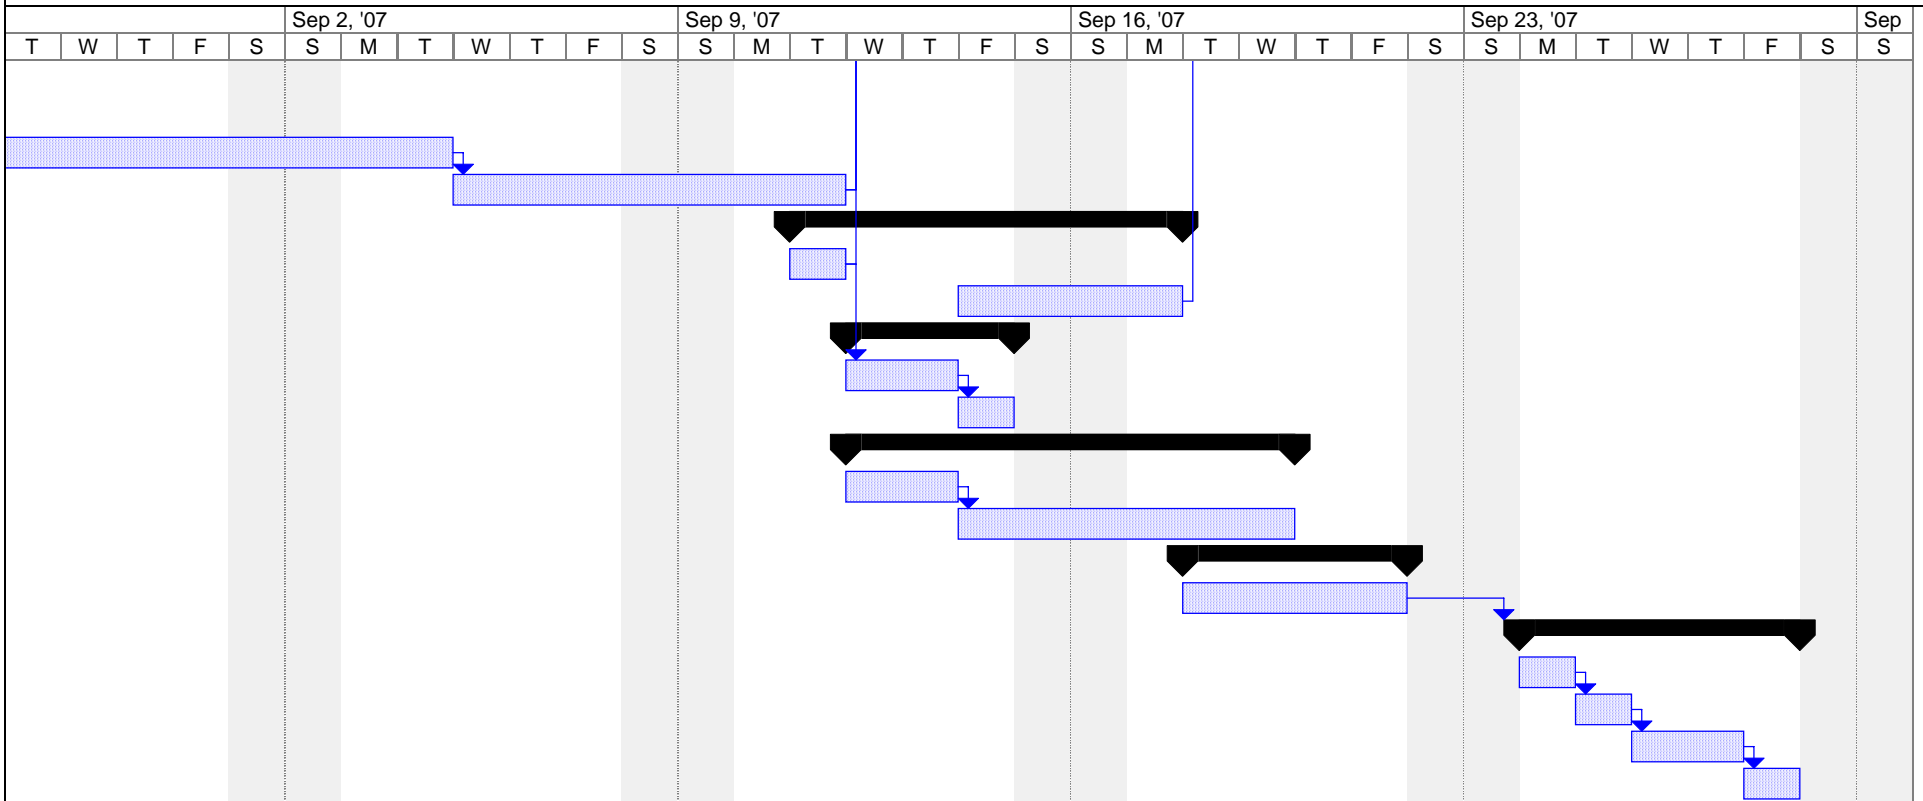

Project: Sweet and Sassy Salon
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
