Activity ID	Activity Name	OD	RD	%	Start	Finish	Total Float
LAUSD - YES Academy - Wellness Center - UP20 W D		784	233		30-Mar-18 A	27-Apr-21	-106
OWNER ITEMS		607	0		03-Apr-18 A	12-Oct-19 A	
		607	0		03-Apr-18 A	12-Oct-19 A	
		607	0		03-Apr-18 A	12-Oct-19 A	
		607	0		03-Apr-18 A	12-Oct-19 A	
MS-01	Notice to Proceed - Preliminary (4/3/18)	0	0	100%	03-Apr-18 A		
MS-02	Change of Project Criteria (4/16/18)	0	0	100%		10-Apr-18 A	
DES1160	Submit Baseline Schedule	72	0	100%	03-May-18 A	02-Aug-18 A	
MS-03	Conduct Field Investigation on Site (5/2/18)	0	0	100%		04-May-18 A	
MS-05	NTP for Design (5/2/18)	0	0	100%		05-May-18 A	
DES1170	Approve Baseline Schedule	18	0	100%	01-Aug-18 A	13-Sep-18 A	
MS-06	Approved Baseline Schedule (7/31/18)	0	0	100%		13-Sep-18 A	
MS-07	DSA Submittal of 100% Construction Document (1/10/19)(2/17/19)	0	0	100%		31-Jan-19 A	
MS-08	DSA Review of Construction Documents (6/10/19)(7/17/19)	0	0	100%		07-Oct-19 A	
MS-09	DSA Approval (6/10/19)(7/18/19)(7/18/19)	0	0	100%		07-Oct-19 A	
MS-19	Issue NTP for Construction	4	0	100%	08-Oct-19 A	11-Oct-19 A	
MS-10	NTP for Construction (6/14/19)(7/22/19)	0	0	100%		12-Oct-19 A	
DESIGN PHASE		545	0		30-Mar-18 A	06-Oct-19 A	
		545	0		30-Mar-18 A	06-Oct-19 A	
		545	0		30-Mar-18 A	06-Oct-19 A	
		545	0		30-Mar-18 A	06-Oct-19 A	
DES1020	Preliminary Schematic Design Submittal	14	0	100%	30-Mar-18 A	12-Apr-18 A	
DES1000	Site Analysis Phase	28	0	100%	04-Apr-18 A	02-May-18 A	
DES1030	LAUSD Reviews - Preliminary Schematics	7	0	100%	13-Apr-18 A	26-Apr-18 A	
DES1040	Final Schematic Design Submittal	14	0	100%	27-Apr-18 A	15-May-18 A	
DES1010	NTP For Design	0	0	100%		07-May-18 A	
DES1050	LAUSD Reviews - Final Schematics	10	0	100%	16-May-18 A	18-Jun-18 A	
DES1060	Design Development Submittal	21	0	100%	19-Jun-18 A	13-Sep-18 A	
DES1070	LAUSD Reviews - Design Development	15	0	100%	13-Sep-18 A	03-Oct-18 A	
DES1080	Construction Documents: 50% Submittal	50	0	100%	03-Oct-18 A	12-Oct-18 A	
DES1090	LAUSD Reviews - 50% CD's	15	0	100%	13-Oct-18 A	02-Nov-18 A	
DES1100	Construction Documents: 100%	50	0	100%	03-Nov-18 A	18-Dec-18 A	
DES1120	LAUSD Reviews - 100% CD's	15	0	100%	19-Dec-18 A	12-Jan-19 A	
DES1130	DB Corrections	24	0	100%	13-Jan-19 A	31-Jan-19 A	

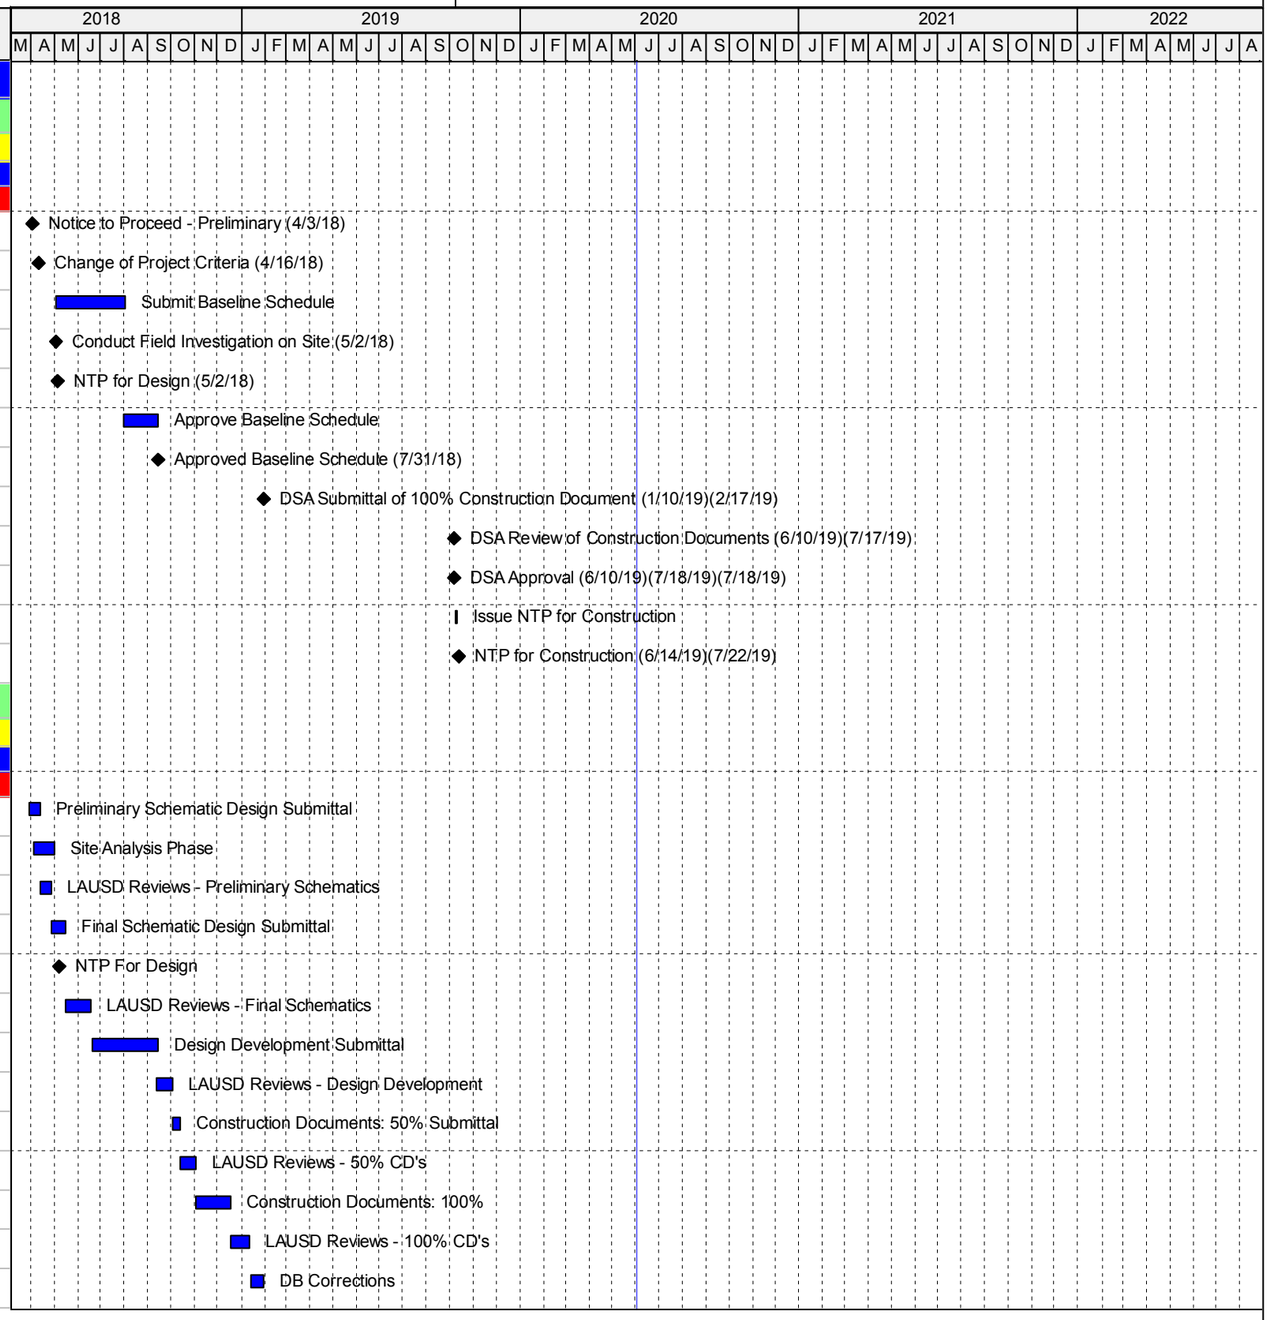

Actual Work ◆ Milestone

Remaining Work

Critical Remaining Work

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	RD	%	Start	Finish	Total Float
DES1140	DSA Plan Check	150	0	100%	01-Feb-19 A	17-Jul-19 A	
DES1140A	Revise & Resubmit for DSA Plan Check	30	0	100%	18-Jul-19 A	06-Oct-19 A	
CHANGE ORDERS		583	5		21-Jun-18 A	05-Jun-20	53
		583	5		21-Jun-18 A	05-Jun-20	53
		583	5		21-Jun-18 A	05-Jun-20	53
		583	5		21-Jun-18 A	05-Jun-20	53
CHNG-001	T-501 Move Building	5	0	100%	21-Jun-18 A	01-Jul-19 A	
CHNG-002	T-502 New Barrier Wall	5	2	50%	21-Jun-18 A	02-Jun-20	56
CHNG-003	T-503 New Card Access Readers	5	2	50%	24-Sep-18 A	02-Jun-20	56
CHNG-004	T-504 Security Glazing	5	5	0%	01-Jun-20	05-Jun-20	53
PRECON		461	233		05-May-18 A	27-Apr-21	-106
BID &AWARD SUBCONTRACTS		198	0		24-Feb-19 A	25-Oct-19 A	
		198	0		24-Feb-19 A	25-Oct-19 A	
		198	0		24-Feb-19 A	25-Oct-19 A	
PP-1282	AMG Preconstruction Service Fee	125	0	100%	24-Feb-19 A	31-Jul-19 A	
PP-1122	Advertisement to Bid	19	0	100%	07-Mar-19 A	25-Mar-19 A	
PP-1132	Job Walk	1	0	100%	21-Mar-19 A	21-Mar-19 A	
PP-1142	RFI Deadline	4	0	100%	22-Mar-19 A	25-Mar-19 A	
PP-1152	Issue an Addendum	3	0	100%	26-Mar-19 A	28-Mar-19 A	
PP-1162	Bid Date	3	0	100%	09-May-19 A	09-May-19 A	
PP-1172	Review bids from Sub-Contractor	14	0	100%	10-May-19 A	20-May-19 A	
PP-1182	Sub-Contractor selection	5	0	100%	21-May-19 A	27-May-19 A	
PP-1192	Issue letter of Intent	1	0	100%	28-May-19 A	28-May-19 A	
PP-1202	Award Sub-Contracts	6	0	100%	29-May-19 A	04-Jul-19 A	
PP-1222	Sub-Contractor Schedule of Values (SOV's)	5	0	100%	04-Jun-19 A	25-Jul-19 A	
PP-1212	Execute Contracts	6	0	100%	04-Jun-19 A	25-Oct-19 A	
PP-1272	Develop Construction Schedule	24	0	100%	04-Jul-19 A	20-Aug-19 A	
PP-1242	Begin Submittals	0	0	100%	12-Jul-19 A		
PP-1252	Submit Construction Schedule	1	0	100%	22-Aug-19 A	22-Aug-19 A	
PP-1232	Sub-Contractor Scheduling Meeting	1	0	100%	22-Aug-19 A	12-Oct-19 A	
PP-1262	LAUSD Approve Construction Schedule	18	0	100%	23-Aug-19 A	23-Aug-19 A	
MATERIAL PROCUREMENT		461	233		05-May-18 A	27-Apr-21	-106
		461	233		05-May-18 A	27-Apr-21	-106
		461	233		05-May-18 A	27-Apr-21	-106
PP-1102	Bonds & Fees	10	0	100%	05-May-18 A	24-Jun-19 A	
PP-130	P/S HM Door Frames	10	0	100%	12-Jul-19 A	12-Jul-19 A	
PP-190	BOA R/A HM Door Frames	10	0	100%	12-Jul-19 A	19-Jul-19 A	

Actual Work ◆ Milestone

Remaining Work

Critical Remaining Work

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	RD	%	Start	Finish	Total Float
PP-250	LAUSD R/A HM Door Frames	18	0	100%	19-Jul-19 A	24-Jul-19 A	
PP-110	P/S Electrical Equipment	10	0	100%	22-Jul-19 A	22-Jul-19 A	
PP-230	LAUSD R/A Electrical Equipment	18	0	100%	22-Jul-19 A	25-Oct-19 A	
PP-170	BOA R/A Electrical Equipment	10	0	100%	22-Jul-19 A	25-Oct-19 A	
PP-1101	General Requirements	351	0	100%	23-Jul-19 A	30-Sep-19 A	
PP-1111	General Conditions	351	331	42%	23-Jul-19 A	27-Apr-21	-153
PP-310	F/D HM Door Frames	35	0	100%	24-Jul-19 A	01-Jun-20	-34
PP-120	P/S Plumbing Eqpt/Fixtures	10	0	100%	25-Jul-19 A	25-Jul-19 A	
PP-180	BOA R/A Plumbing Eqpt/Fixtures	10	0	100%	25-Jul-19 A	25-Oct-19 A	
PP-150	P/S Structural System	10	0	100%	01-Aug-19 A	01-Aug-19 A	
PP-210	BOA R/A Structural System	10	0	100%	01-Aug-19 A	15-Jan-20 A	
PP-270	LAUSD R/A Structural System	18	0	100%	01-Aug-19 A	14-Feb-20 A	
PP-330	F/D Structural System	30	0	100%	01-Aug-19 A	04-May-20 A	
PP-100	P/S Mechanical Equipment	10	0	100%	07-Aug-19 A	07-Aug-19 A	
PP-160	BOA R/A Mechanical Equipment	10	0	100%	07-Aug-19 A	28-Feb-20 A	
PP-240	LAUSD R/A Plumbing Eqpt/Fixtures	18	0	100%	25-Oct-19 A	07-Nov-19 A	
PP-290	F/D Electrical Equipment	45	36	20%	25-Oct-19 A	20-Jul-20	-33
PP-220	LAUSD R/A Mechanical Equipment	18	0	100%	29-Oct-19 A	28-Feb-20 A	
PP-280	F/D Mechanical Equipment	45	42	5%	29-Oct-19 A	28-Jul-20	-34
PP-140	P/S Storefront System	10	0	100%	04-Nov-19 A	04-Nov-19 A	
PP-260	LAUSD R/A Storefront System	16	0	100%	04-Nov-19 A	01-Jun-20	-34
PP-200	BOA R/A Storefront System	10	0	100%	04-Nov-19 A	01-Jun-20	-34
PP-320	F/D Storefront System	35	35	0%	04-Nov-19 A	17-Jul-20	-34
PP-300	F/D Plumbing Eqpt/Fixtures	35	35	0%	02-Mar-20 A	17-Jul-20	-23
EARLY WORK		116	0		07-Jun-19 A	31-Oct-19 A	
		116	0		07-Jun-19 A	31-Oct-19 A	
Mobilization		116	0		07-Jun-19 A	31-Oct-19 A	
MOB-0500	Trailer Delivery	1	0	100%	07-Jun-19 A	07-Jun-19 A	
MOB-0505	Temporary Fencing (Construction Site)	1	0	100%	07-Jun-19 A	07-Jun-19 A	
MOB-0515	Set Up Trailers	3	0	100%	10-Jun-19 A	12-Jun-19 A	
MOB-0510	Temporary Toilets & Wash Stations	1	0	100%	25-Jun-19 A	25-Jun-19 A	
MOB-0520	Temporary Signage (Construction Site)	1	0	100%	25-Jun-19 A	25-Jun-19 A	
MOB-0526	Provide Temporary Path of Travel	3	0	100%	25-Jun-19 A	25-Jun-19 A	
MOB-0525	Remove Trees	2	0	100%	30-Jul-19 A	30-Jul-19 A	
MOB-0575	Temporary Water	2	0	100%	09-Aug-19 A	16-Oct-19 A	

Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	RD	%	Start	Finish	Total Float
MOB-0530	Temporary Power	2	0	100%	26-Aug-19 A	31-Oct-19 A	
MOB-0535	Temporary Data	9	0	100%	01-Oct-19 A	04-Oct-19 A	
PHASE 1		212	22		14-Aug-19 A	30-Jun-20	52
PARKING LOT & SITEWORK		212	22		14-Aug-19 A	30-Jun-20	52
PARKING LOT		212	22		14-Aug-19 A	30-Jun-20	52
		186	22		29-Oct-19 A	30-Jun-20	52
PL-2020	Light Pole Bases	4	0	100%	29-Oct-19 A	03-Mar-20 A	
PL-2030	Curb & Gutter	4	0	100%	29-Oct-19 A	10-Mar-20 A	
PL-2010	U/G Electrical Lighting	3	0	100%	05-Nov-19 A	18-Nov-19 A	
PL-2040	Install Landscape Irrigation	9	0	100%	07-Nov-19 A	18-May-20 A	
PL-2050	Form Site Flatwork	2	0	100%	02-Mar-20 A	15-May-20 A	
PL-2060	Rebar Site Flatwork	2	0	100%	02-Mar-20 A	15-May-20 A	
PL-2000	Site Fine Grading	7	0	100%	03-Mar-20 A	01-Apr-20 A	
PL-2070	Place Site Flatwork	2	0	100%	04-Mar-20 A	18-May-20 A	
PL-2090	Base & Asphalt Paving	5	0	100%	02-Apr-20 A	03-Apr-20 A	
PL-2080	Set & Connect Light poles	2	0	100%	10-Apr-20 A	15-Apr-20 A	
PL-2110	Landscaping & Planting	9	0	100%	06-May-20 A	18-May-20 A	
PL-2100	Seal & Striping	1	1	0%	07-May-20 A	01-Jun-20	41
PL-2130	Punchlist - Phase 1	5	3	40%	29-May-20 A	03-Jun-20	-105
MS-22	Construction Closeout - Phase 1	30	30	0%	01-Jun-20	30-Jun-20	74
MS-32	Turnover Phase 1 to LAUSD	1	1	0%	03-Jun-20	03-Jun-20	-105
Mobilization		13	0		14-Aug-19 A	20-Feb-20 A	
MOB-0555	Protect Exisiting Utilites	1	0	100%	14-Aug-19 A	16-Aug-19 A	
MOB-0545	Layout for Demolition	1	0	100%	09-Oct-19 A	23-Oct-19 A	
MOB-0560	Clear and grub	2	0	100%	15-Oct-19 A	16-Oct-19 A	
MOB-0540	Protect In Place Exisiting (Pedestrian Gates, Solar Lights)	1	0	100%	15-Oct-19 A	18-Oct-19 A	
MOB-0550	Protect in Place Trees	1	0	100%	15-Oct-19 A	12-Nov-19 A	
MOB-0570	Demolition	5	0	100%	16-Oct-19 A	22-Oct-19 A	
MOB-0580	Survey for Grading	1	0	100%	23-Oct-19 A	29-Oct-19 A	
MOB-0565	Install Erosion Control System	2	0	100%	24-Oct-19 A	24-Oct-19 A	
MOB-0585	Deliver Storage Containers	1	0	100%	25-Oct-19 A	25-Oct-19 A	
MOB-0590	Deliver Dumpsters	1	0	100%	25-Oct-19 A	25-Oct-19 A	
MOB-590	Remove / Export Soils	3	0	100%	25-Oct-19 A	20-Feb-20 A	
PHASE 2		247	233		28-Apr-20 A	27-Apr-21	-106
GRADING & SITE UTILITIES		39	25		28-Apr-20 A	03-Jul-20	-17
		39	25		28-Apr-20 A	03-Jul-20	-17

Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	RD	%	Start	Finish	Total Float
		39	25		28-Apr-20 A	03-Jul-20	-17
SU-1070	Demo / Clear & Grub	3	6	0%	28-Apr-20 A	08-Jun-20	-108
SU-1010	Overexc / Recompact	7	7	0%	09-Jun-20	17-Jun-20	-108
SU-1080	Certify Bldg Pad	1	1	0%	18-Jun-20	18-Jun-20	-108
SU-1050	Site Grading for Phase 2	3	3	0%	19-Jun-20	23-Jun-20	-17
PL-2160	U/G Storm Dain	3	3	0%	24-Jun-20	26-Jun-20	-12
PL-2140	U/G Fire/Dom Water	4	4	0%	24-Jun-20	29-Jun-20	-13
SU-1030	Site U/G Electrical Power	5	5	0%	24-Jun-20	30-Jun-20	-14
SU-1040	Site U/G Electrical Data	5	5	0%	24-Jun-20	30-Jun-20	-14
PL-2150	U/G Sewer	8	8	0%	24-Jun-20	03-Jul-20	-17
BUILDING		125	125		19-Jun-20	14-Dec-20	-107
FOUNDATIONS		30	30		19-Jun-20	30-Jul-20	-108
FOOTING		15	15		19-Jun-20	09-Jul-20	-108
FDN-1000	Building Control	1	1	0%	19-Jun-20	19-Jun-20	-108
FDN-1010	U/G Plumbing	5	5	0%	22-Jun-20	26-Jun-20	-108
FDN-1020	U/G Electrical	4	4	0%	23-Jun-20	26-Jun-20	-108
FDN-1030	Excavate for Footings	3	3	0%	29-Jun-20	01-Jul-20	-108
FDN-1040	Rebar For Footings	5	5	0%	30-Jun-20	06-Jul-20	-108
FDN-1060	Form for Footings	5	5	0%	01-Jul-20	07-Jul-20	-108
FDN-1090	Bolt Templates / AB	2	2	0%	03-Jul-20	06-Jul-20	-107
FDN-1100	Place Concrete Footings	2	2	0%	08-Jul-20	09-Jul-20	-108
SLAB ON GRADE		15	15		10-Jul-20	30-Jul-20	-108
FDN-1150	Radon System	5	5	0%	10-Jul-20	16-Jul-20	-108
FDN-1050	Vapor Barrier	2	2	0%	16-Jul-20	17-Jul-20	-108
FDN-1070	In-Slab Plumbing	2	2	0%	20-Jul-20	21-Jul-20	-108
FDN-1080	In-Slab Elect/Data	2	2	0%	20-Jul-20	21-Jul-20	-108
FDN-1120	Rebar SOG	2	2	0%	22-Jul-20	23-Jul-20	-108
FDN-1160	Place Concrete SOG	2	2	0%	24-Jul-20	27-Jul-20	-108
FDN-1110	Strip / Clean / Sawcut	3	3	0%	28-Jul-20	30-Jul-20	-108
STRUCTURAL		19	19		31-Jul-20	26-Aug-20	-108
		19	19		31-Jul-20	26-Aug-20	-108
STR-1000	Erect Steel	10	10	0%	31-Jul-20	13-Aug-20	-108
STR-1010	Bolt & Weld Steel	7	7	0%	11-Aug-20	19-Aug-20	-108
STR-1020	Metal Decking	5	5	0%	20-Aug-20	26-Aug-20	-108
EXTERIOR		60	60		27-Aug-20	19-Nov-20	-106
		60	60		27-Aug-20	19-Nov-20	-106
EX-1000	Metal Stud Framing @ Exterior	10	10	0%	27-Aug-20	10-Sep-20	-107

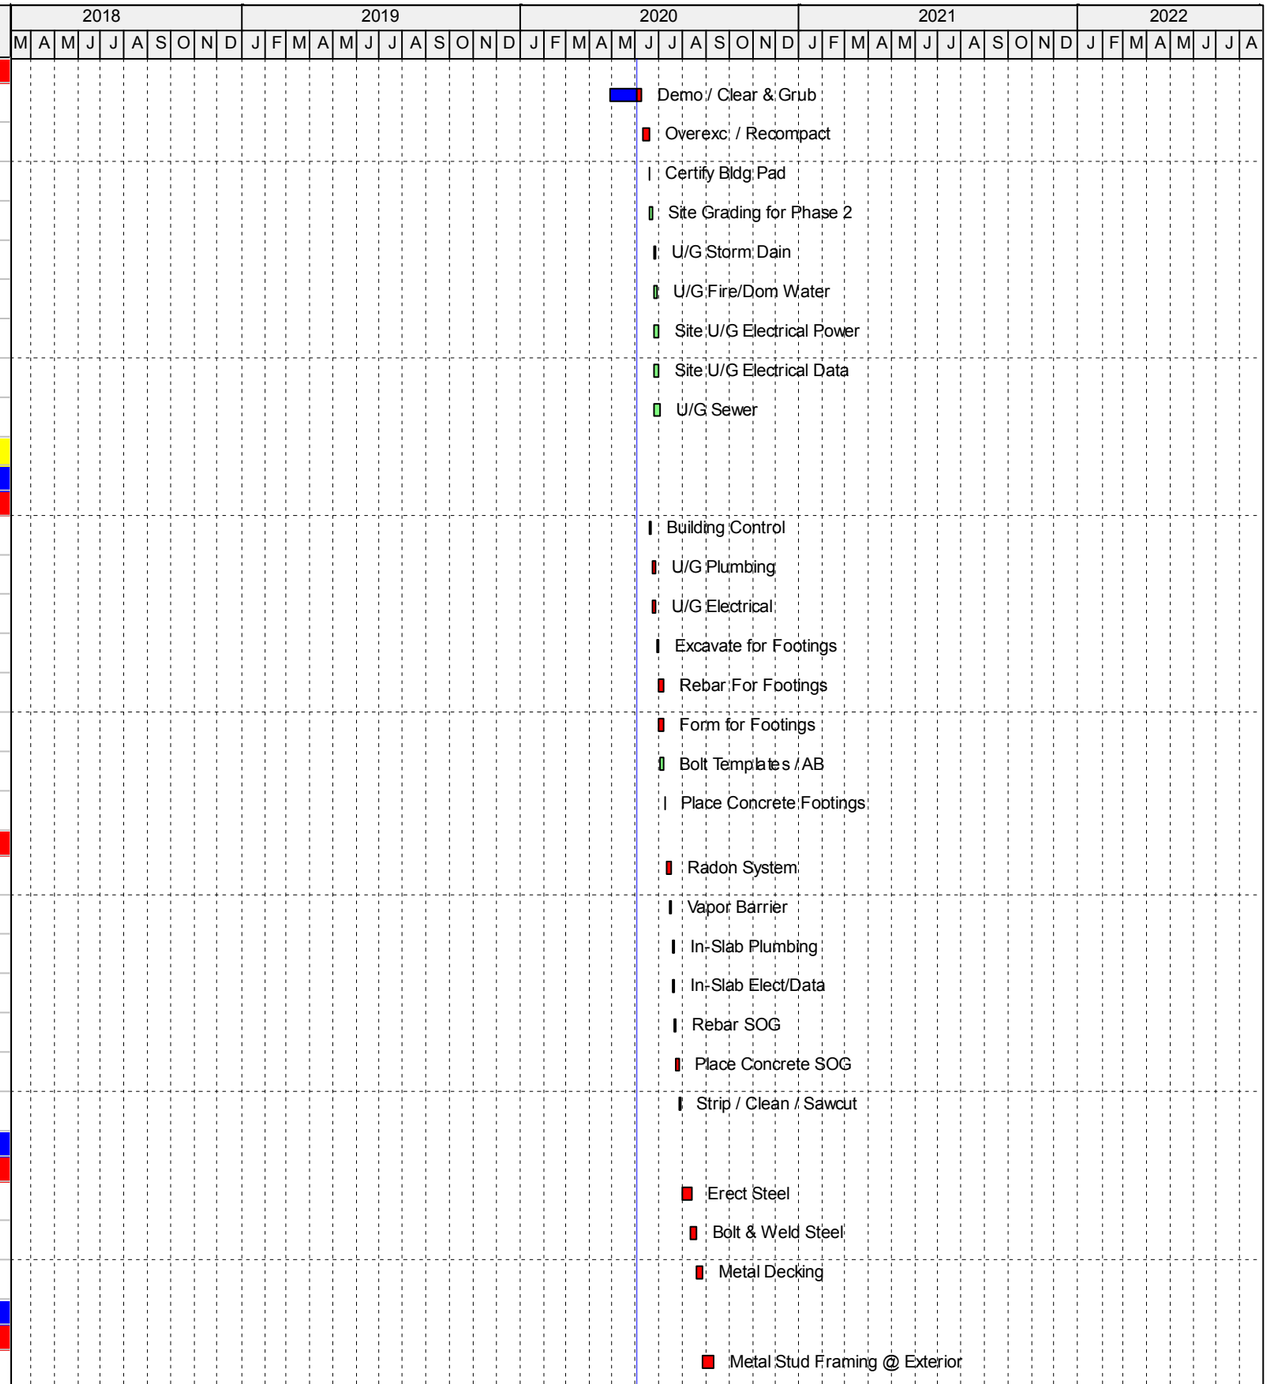

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	RD	%	Start	Finish	Total Float
EX-1010	Exterior Plywood Sheathing	5	5	0%	03-Sep-20	10-Sep-20	-105
EX-1050	Solar Shade Supports	2	2	0%	11-Sep-20	14-Sep-20	-104
EX-1040	Install HM Window/Storefront Frames	3	3	0%	11-Sep-20	15-Sep-20	-105
EX-1030	Install Door HM Frames	5	5	0%	11-Sep-20	17-Sep-20	-107
EX-1060	Exterior SM Pre-Flashing	3	3	0%	18-Sep-20	22-Sep-20	-107
EX-1070	Rigid Foam Insulation	4	4	0%	23-Sep-20	28-Sep-20	-107
EX-1250	Set-Up Scaffold	3	3	0%	25-Sep-20	29-Sep-20	-107
EX-1080	Vapor Barrier / Lath	5	5	0%	29-Sep-20	05-Oct-20	-107
EX-1090	Exterior Dry-in	0	0	0%		05-Oct-20	-107
EX-1100	Scratch Coat	1	1	0%	09-Oct-20	09-Oct-20	-107
EX-1110	Cure Scratch Coat	2	2	0%	12-Oct-20	13-Oct-20	-107
EX-1120	Brown Coat	3	3	0%	14-Oct-20	16-Oct-20	-107
EX-1130	Cure Brown Coat	5	5	0%	19-Oct-20	23-Oct-20	-107
EX-1140	Finish Coat	3	3	0%	26-Oct-20	28-Oct-20	-107
EX-1150	Remove Scaffold	1	1	0%	29-Oct-20	29-Oct-20	-107
EX-1160	Install Exterior Doors	2	2	0%	30-Oct-20	02-Nov-20	-107
EX-1240	Install Storefront	2	2	0%	30-Oct-20	02-Nov-20	-107
EX-1170	Paint Exterior	5	5	0%	03-Nov-20	09-Nov-20	-107
EX-1210	Exterior Light Fixtures	1	1	0%	10-Nov-20	10-Nov-20	-99
EX-1200	Building Signage	2	2	0%	10-Nov-20	11-Nov-20	-100
EX-1220	Install Solar Shade Finish	3	3	0%	10-Nov-20	12-Nov-20	-101
EX-1180	Exterior SM Post-Flashing (Incl Corrug Mtl @ Entry)	4	4	0%	10-Nov-20	13-Nov-20	-102
EX-1190	Install Window Glazing	5	5	0%	10-Nov-20	16-Nov-20	-106
EX-1230	Exterior Security Window Screens	3	3	0%	17-Nov-20	19-Nov-20	-106
ROOF		27	27		27-Aug-20	05-Oct-20	-73
		27	27		27-Aug-20	05-Oct-20	-73
RF-1010	Install Roof Hatch	1	1	0%	27-Aug-20	27-Aug-20	-92
RF-1000	Install Mechanical Curbs	2	2	0%	27-Aug-20	28-Aug-20	-93
RF-1030	Electrical Penetrations	2	2	0%	27-Aug-20	28-Aug-20	-93
RF-1040	Plumbing Penetrations	3	3	0%	27-Aug-20	31-Aug-20	-94
RF-1060	Install Solatubes/Skylights	4	4	0%	27-Aug-20	01-Sep-20	-95
RF-1020	Mechanical Penetrations	5	5	0%	27-Aug-20	02-Sep-20	-96
RF-1050	Set Mech Screen	5	5	0%	27-Aug-20	02-Sep-20	-96
RF-1070	Rigid Insulation / Densdeck	3	3	0%	11-Sep-20	15-Sep-20	-101

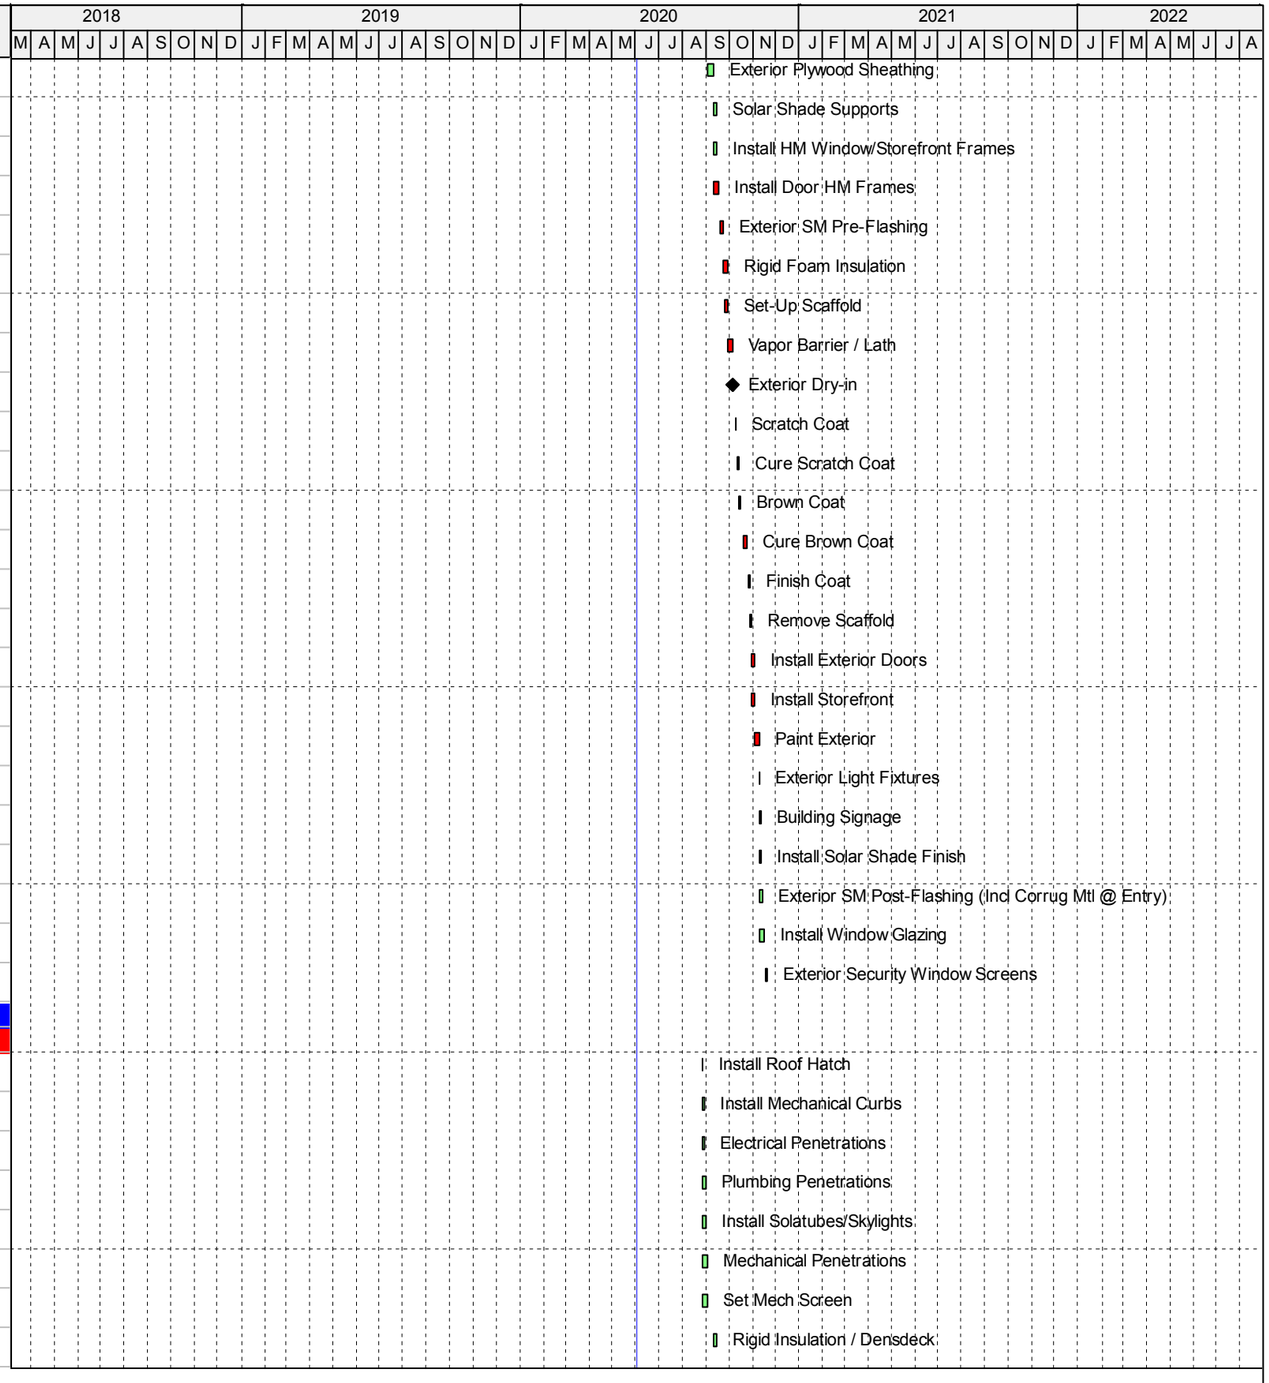

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	RD	%	Start	Finish	Total Float
RF-1080	Single Ply Roof	7	7	0%	16-Sep-20	24-Sep-20	-101
RF-1090	Roof Dry-in	0	0	0%		24-Sep-20	-101
RF-1100	Set Mechanical Eqpt	2	2	0%	25-Sep-20	28-Sep-20	-75
RF-1110	Reglet & SM Flashing	5	5	0%	25-Sep-20	01-Oct-20	-85
RF-1120	Plumbing Hookup	2	2	0%	29-Sep-20	30-Sep-20	-72
RF-1130	Electrical Hookup	5	5	0%	29-Sep-20	05-Oct-20	-75
RF-1140	Mechanical Hookup	5	5	0%	29-Sep-20	05-Oct-20	-75
RF-1150	Install Walkway Pads	2	2	0%	02-Oct-20	05-Oct-20	-73
ROUGH-INS		32	32		25-Aug-20	08-Oct-20	-108
		32	32		25-Aug-20	08-Oct-20	-108
IR-1000	Layout for Rough-ins	1	1	0%	25-Aug-20	25-Aug-20	-108
IR-1090	Install Toptrack	5	5	0%	26-Aug-20	01-Sep-20	-108
IR-1010	Rough-in - O/H Mechanical Mains	12	12	0%	28-Aug-20	15-Sep-20	-108
IR-1030	Rough-in - O/H Plumbing	3	3	0%	09-Sep-20	11-Sep-20	-102
IR-1020	Rough-in - O/H Fire Protection Mains	7	7	0%	09-Sep-20	17-Sep-20	-103
IR-1040	Rough-in - O/H Mechanical Laterals	12	12	0%	14-Sep-20	29-Sep-20	-108
IR-1050	Frame Interior Metal Stud Walls/Shear Walls	10	10	0%	16-Sep-20	29-Sep-20	-106
IR-1070	Rough-in - Plumbing In Walls	10	10	0%	18-Sep-20	01-Oct-20	-106
IR-1060	Rough-in - Elect / LV - OH/Walls	10	10	0%	22-Sep-20	05-Oct-20	-105
IR-1080	Rough-in - O/H Fire Protection Laterals	7	7	0%	30-Sep-20	08-Oct-20	-108
DRYWALL - WALLS & CEILINGS		19	19		02-Oct-20	28-Oct-20	-108
		19	19		02-Oct-20	28-Oct-20	-108
IF-1000	Insulate Walls / Ceilings	5	5	0%	02-Oct-20	08-Oct-20	-106
IF-1010	Hang Drywall Walls	7	7	0%	06-Oct-20	14-Oct-20	-107
IF-1020	Install Suspended Hardlid Ceiling	5	5	0%	09-Oct-20	15-Oct-20	-108
IF-3180	Tape & Finish Walls	10	10	0%	09-Oct-20	22-Oct-20	-105
IF-1040	Rough-in Elect in Hardlids	4	4	0%	16-Oct-20	21-Oct-20	-108
IF-1050	Rough-in Mech in Hardlids	4	4	0%	16-Oct-20	21-Oct-20	-108
IF-1060	Rough-in Fire Protection in Hardlids	4	4	0%	16-Oct-20	21-Oct-20	-108
IF-1070	Hang Drywall @ Suspended Lid Ceilings	3	3	0%	21-Oct-20	23-Oct-20	-108
IF-1030	Tape & Finish Hardlids	3	3	0%	26-Oct-20	28-Oct-20	-108
SUSPENDED CEILINGS		17	17		28-Oct-20	19-Nov-20	-105
		17	17		28-Oct-20	19-Nov-20	-105
IF-2000	Prime Paint	5	5	0%	28-Oct-20	03-Nov-20	-108
IF-2010	Install Suspended T-Bar Ceiling System	7	7	0%	02-Nov-20	10-Nov-20	-106
IF-2020	Install Suspended Wood Plank Ceiling System	5	5	0%	04-Nov-20	10-Nov-20	-107

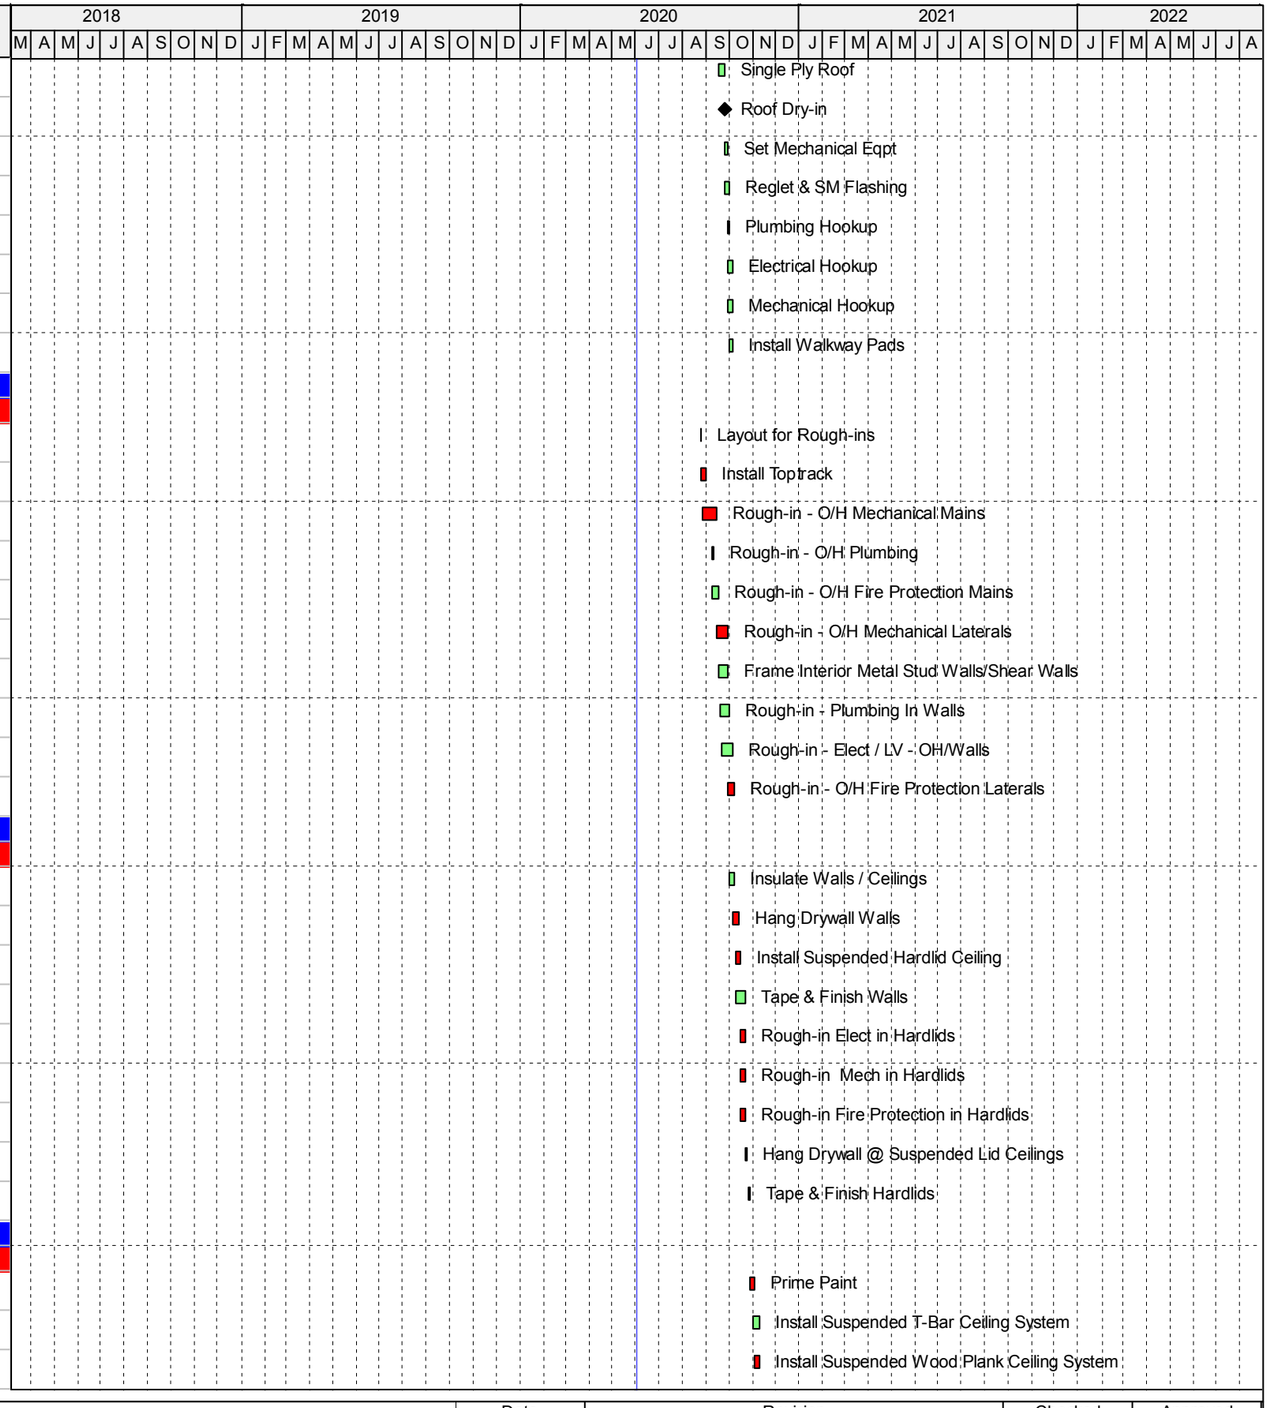

Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	RD	%	Start	Finish	Total Float
IF-2030	Rough-in Elect in Suspended Ceiling System	6	6	0%	09-Nov-20	16-Nov-20	-107
IF-2040	Rough-in Mech in Suspended Ceiling System	6	6	0%	09-Nov-20	16-Nov-20	-107
IF-2050	Rough-in Fire Protection in Suspended Ceiling System	6	6	0%	09-Nov-20	16-Nov-20	-107
IF-2060	Install Wooden Ceiling Planks	5	5	0%	13-Nov-20	19-Nov-20	-105
IF-2070	Drop Acoustical Ceiling Tiles	3	3	0%	17-Nov-20	19-Nov-20	-107
ELECTRICAL ROOM		101	101		01-Jul-20	19-Nov-20	-108
		101	101		01-Jul-20	19-Nov-20	-108
ER-1000	Connect LV Conduits to (E) Telecom Bldg	5	5	0%	01-Jul-20	07-Jul-20	-14
ER-1010	Set Electrical Panels	2	2	0%	04-Nov-20	05-Nov-20	-108
ER-1020	Pull LV from (E) to New Elect Rm	2	2	0%	04-Nov-20	05-Nov-20	-98
ER-1030	Pull Feeder Wire	2	2	0%	06-Nov-20	09-Nov-20	-108
ER-1040	Pull & Terminate Bldg Wire	9	9	0%	06-Nov-20	18-Nov-20	-108
ER-1050	Energize Electrical	1	1	0%	19-Nov-20	19-Nov-20	-108
FINISHES		28	28		04-Nov-20	14-Dec-20	-107
		28	28		04-Nov-20	14-Dec-20	-107
IF-3000	Ceramic Tile	8	8	0%	04-Nov-20	13-Nov-20	-107
IF-3010	Plumbing Eqpt & Finishes	7	7	0%	16-Nov-20	24-Nov-20	-107
IF-3030	Final Paint	6	6	0%	20-Nov-20	30-Nov-20	-107
IF-3050	Countertops	3	3	0%	24-Nov-20	27-Nov-20	-107
IF-3040	Casework	5	5	0%	24-Nov-20	01-Dec-20	-107
IF-3020	Toilet Accessories	2	2	0%	25-Nov-20	27-Nov-20	-107
IF-3100	Install Mechanical Trim	3	3	0%	30-Nov-20	02-Dec-20	-107
IF-3110	Install Electrical trim	3	3	0%	30-Nov-20	02-Dec-20	-107
IF-3060	Hang Doors & Hardware	3	3	0%	02-Dec-20	04-Dec-20	-106
IF-3070	Install Interior Signage	3	3	0%	02-Dec-20	04-Dec-20	-106
IF-3080	Set Fire Extinguishers	3	3	0%	02-Dec-20	04-Dec-20	-106
IF-3090	Install Window Coverings	3	3	0%	02-Dec-20	04-Dec-20	-106
IF-3140	Install Visual Display Boards	3	3	0%	02-Dec-20	04-Dec-20	-106
IF-3120	Install Plumbing Trim	3	3	0%	03-Dec-20	07-Dec-20	-107
IF-3130	Install Fire Sprinkler Trim	3	3	0%	03-Dec-20	07-Dec-20	-107
IF-3150	Entry Floor Mats	3	3	0%	03-Dec-20	07-Dec-20	-107
IF-3160	Install LVT	5	5	0%	08-Dec-20	14-Dec-20	-107
IF-3170	Install Resilient Sheet Vinyl	5	5	0%	08-Dec-20	14-Dec-20	-107
PARKING LOT & SITEWORK		42	42		19-Oct-20	16-Dec-20	-99
PARKING LOT		33	33		19-Oct-20	03-Dec-20	-90
		33	33		19-Oct-20	03-Dec-20	-90

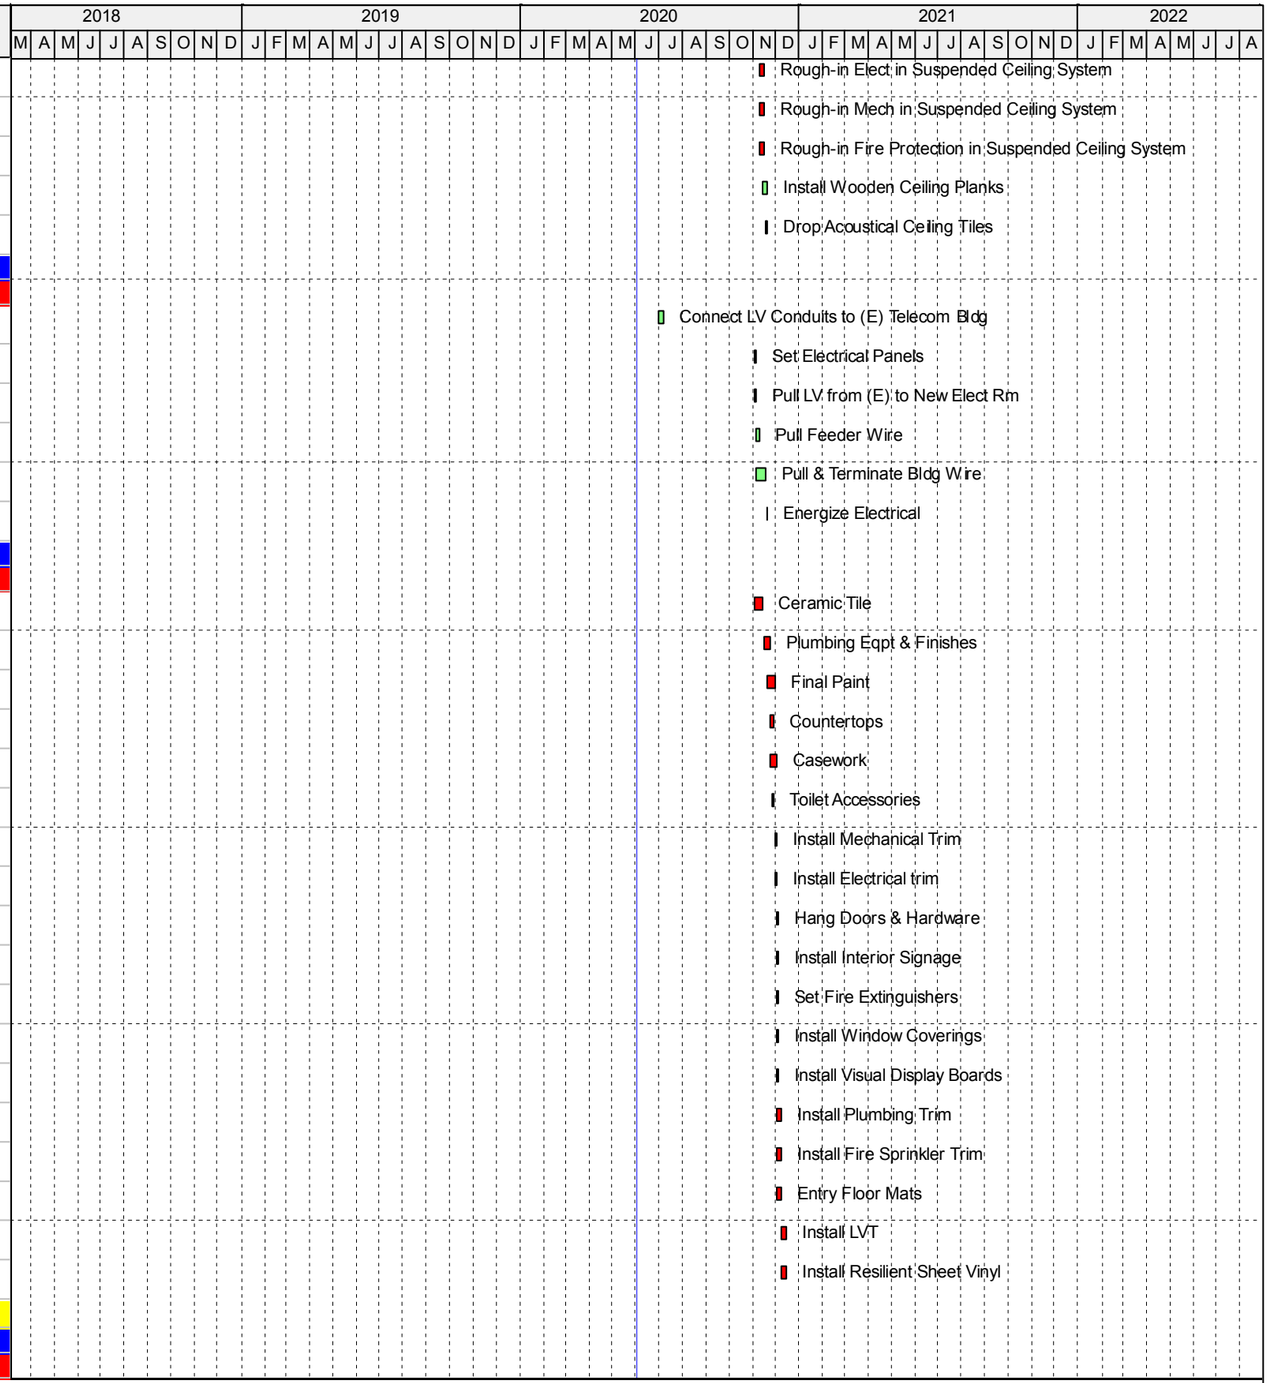

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	RD	%	Start	Finish	Total Float
PL-1000	Rough Grading	2	2	0%	19-Oct-20	20-Oct-20	-91
PL-1010	U/G Electrical Lighting	3	3	0%	21-Oct-20	23-Oct-20	-91
PL-1020	Light Pole Bases	3	3	0%	21-Oct-20	23-Oct-20	-91
PL-1030	Curb & Gutter	5	5	0%	26-Oct-20	30-Oct-20	-91
PL-1050	Form Site Flatwork	2	2	0%	02-Nov-20	03-Nov-20	-91
PL-1060	Rebar Site Flatwork	2	2	0%	04-Nov-20	05-Nov-20	-91
PL-1070	Place Site Flatwork	2	2	0%	06-Nov-20	09-Nov-20	-91
PL-1080	Set & Connect Light poles	2	2	0%	10-Nov-20	11-Nov-20	-90
PL-1090	Base & Asphal Paving	5	5	0%	12-Nov-20	18-Nov-20	-90
PL-1100	Seal & Striping	1	1	0%	19-Nov-20	19-Nov-20	-86
PL-1110	install Signage	5	5	0%	19-Nov-20	25-Nov-20	-90
PL-1120	Punchlist	5	5	0%	27-Nov-20	03-Dec-20	-90
SITEWORK		26	26		10-Nov-20	16-Dec-20	-106
General		26	26		10-Nov-20	16-Dec-20	-106
SW-1000	Install Landscape Irrigation	5	5	0%	10-Nov-20	16-Nov-20	-107
SW-1040	Install Masonry @ Site	5	5	0%	20-Nov-20	27-Nov-20	-107
SW-1090	Site Signage	3	3	0%	03-Dec-20	07-Dec-20	-107
SW-1080	Install Fencing & Gates	5	5	0%	03-Dec-20	09-Dec-20	-107
SW-1100	Landscaping & Planting	5	5	0%	10-Dec-20	16-Dec-20	-106
Trash Enclosure		11	11		17-Nov-20	02-Dec-20	-107
SW-1010	Form Site Footing	1	1	0%	17-Nov-20	17-Nov-20	-107
SW-1020	Rebar Site Footings	1	1	0%	18-Nov-20	18-Nov-20	-107
SW-1030	Place Site Footing	1	1	0%	19-Nov-20	19-Nov-20	-107
SW-1050	Form Site Flatwork	1	1	0%	30-Nov-20	30-Nov-20	-107
SW-1060	Rebar Site Flatwork	1	1	0%	01-Dec-20	01-Dec-20	-107
SW-1070	Place Site Flatwork	1	1	0%	02-Dec-20	02-Dec-20	-107
Drive Way Approach		5	5		16-Nov-20	20-Nov-20	-100
SW-1110	Demo (E) Driveway Approach	1	1	0%	16-Nov-20	16-Nov-20	-100
SW-1120	Form & Base - Driveway Approach	2	2	0%	17-Nov-20	18-Nov-20	-100
SW-1130	Rebar Driveway Approach	1	1	0%	19-Nov-20	19-Nov-20	-100
SW-1140	Place Driveway Approach	1	1	0%	20-Nov-20	20-Nov-20	-100
CLOSEOUT		159	159		20-Nov-20	27-Apr-21	-153
		159	159		20-Nov-20	27-Apr-21	-153
		159	159		20-Nov-20	27-Apr-21	-153
CO-6020	Start-up Eqpt	12	12	0%	20-Nov-20	01-Dec-20	-152
CO-6010	AMG Punch List	21	21	0%	24-Nov-20	14-Dec-20	-153

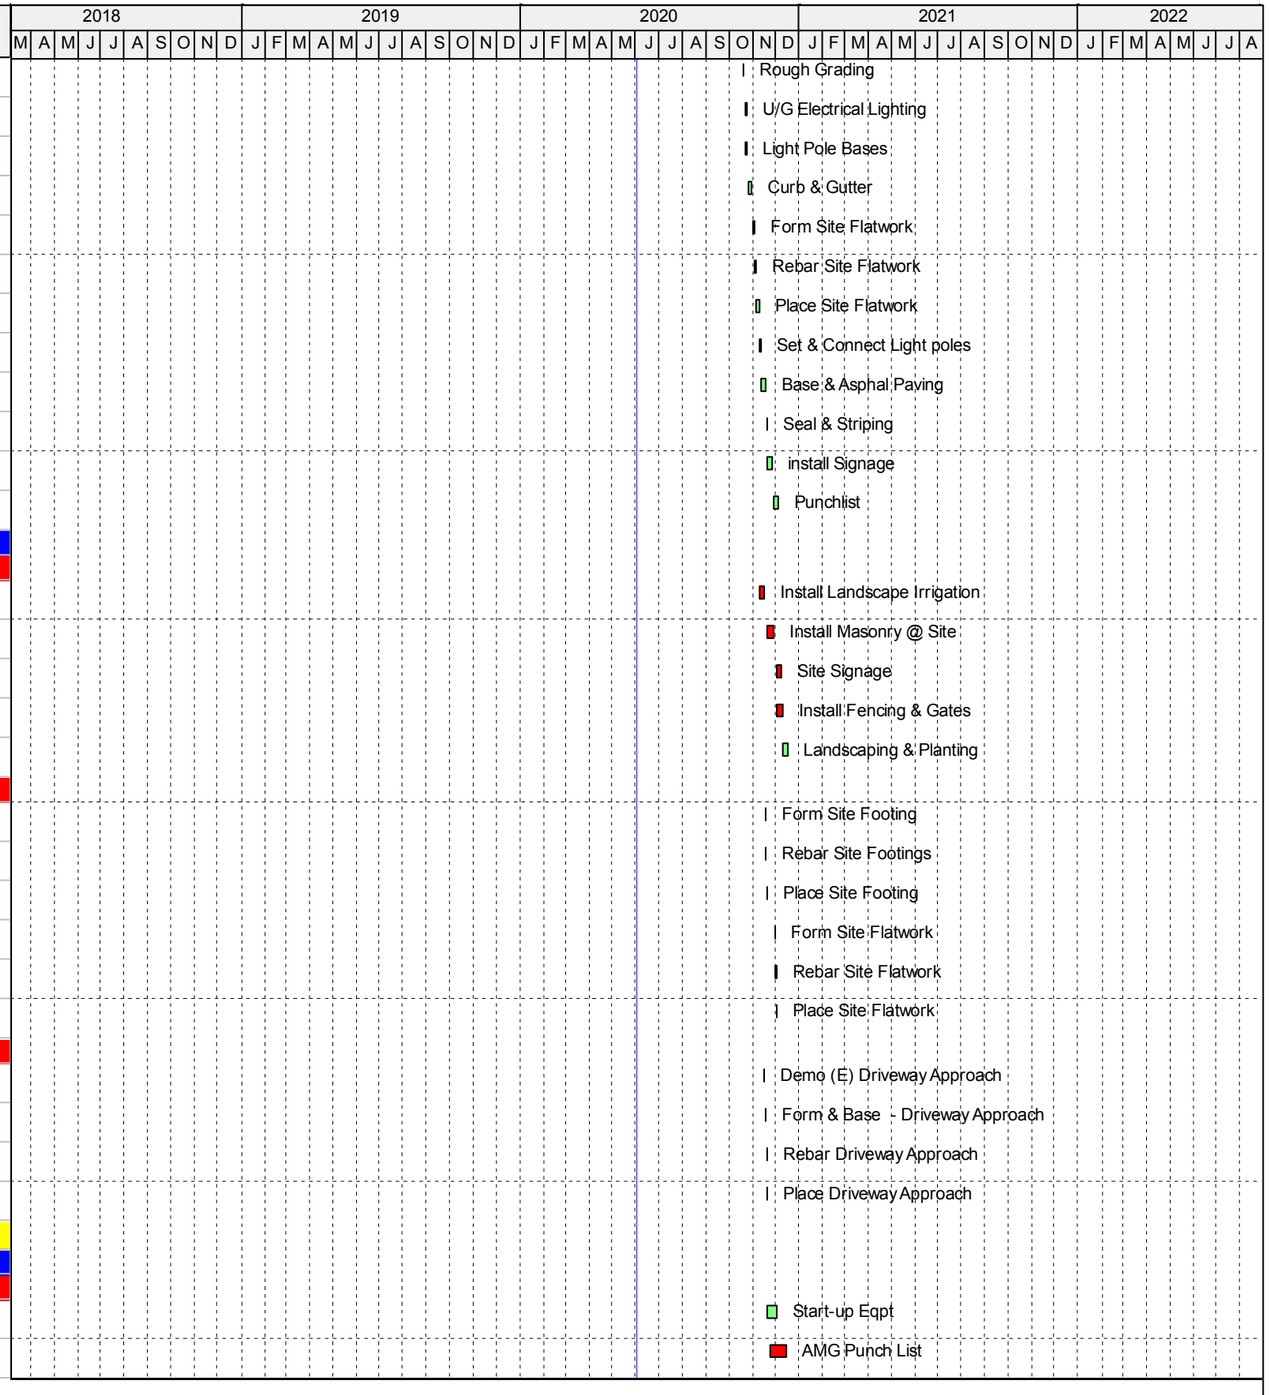

Actual Work ◆ Milestone

Remaining Work

Critical Remaining Work

Date	Revision	Checked	Approved

Activity ID	Activity Name	OD	RD	%	Start	Finish	Total Float
CO-6000	Testing, Balancing of Systems	4	4	0%	03-Dec-20	06-Dec-20	-153
CO-6030	Fire Alarm Testing	3	3	0%	07-Dec-20	09-Dec-20	-143
CO-6005	Commissioning & Training of Systems	12	12	0%	08-Dec-20	19-Dec-20	-153
CO-6050	Owner Punch List	10	10	0%	15-Dec-20	24-Dec-20	-153
CO-6060	Fire / Lfe / Safety Inspections	5	5	0%	20-Dec-20	24-Dec-20	-153
MS-24	Weather Allowance	4	4	0%	25-Dec-20	28-Dec-20	-153
MS-14	Substantial Completion	0	0	0%		28-Dec-20*	-153
MS-13	Phase 2 Construction	0	0	0%		28-Dec-20*	-152
CO-6015	O & M / As-Builts / Warranty Info	14	14	0%	29-Dec-20	11-Jan-21	-107
CO-6040	FINAL Construction Completion	60	60	0%	29-Dec-20	26-Feb-21	-153
MS-15	FINAL Construction Completion	0	0	0%		26-Feb-21*	-153
DP-1045	Design Close Out/Project Certification	60	60	0%	27-Feb-21	27-Apr-21	-153
MS-16	Final Design Closeout & Project Certification:	0	0	0%		27-Apr-21*	-153
MS-17	Contract Completion	0	0	0%		27-Apr-21*	-153

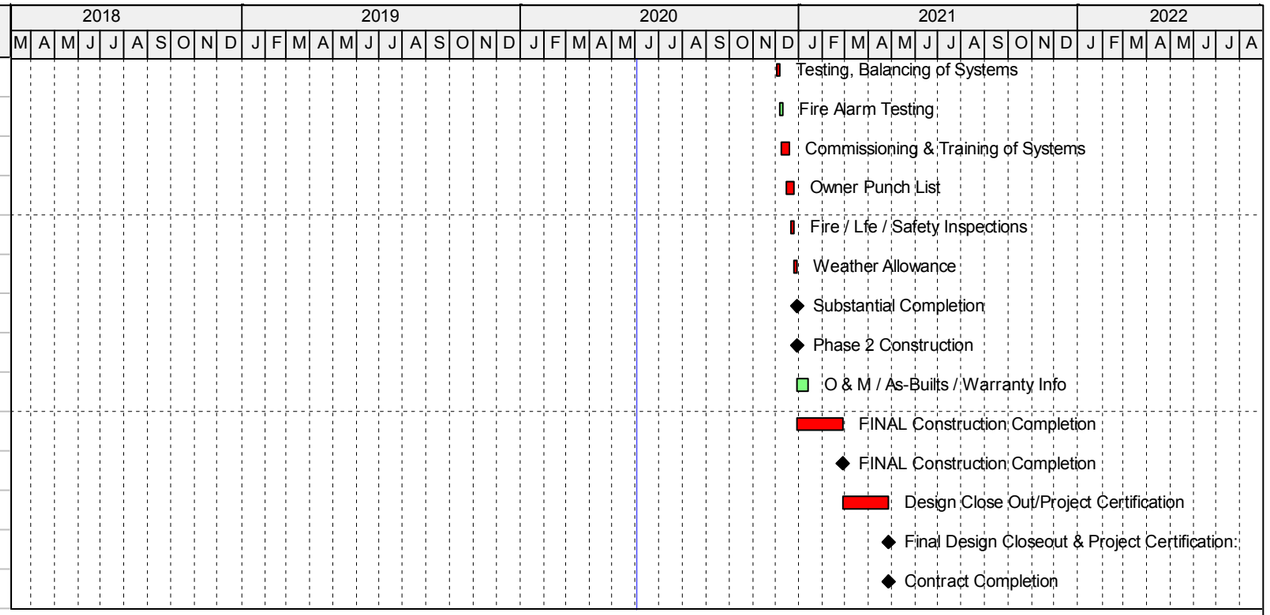

Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Date	Revision	Checked	Approved
